



TADA v2 – Business Requirement Document (BRD)

TADA v2 – Business Requirement Document (BRD)

Transforming Content Platform into Fintech-Driven Monetization Ecosystem

Prepared by: Dean (Business Analyst → Product Owner)

1. Executive Overview

TADA started as a **comic and storytelling sharing platform** (webtoon, novel). From **mid-2024**, the company and the **Indonesian investor** decided to build **TADA v2** — a **Fintech + Content** ecosystem featuring:

- **Automated revenue sharing system** for Creator & User
- Internal E-Wallet
- Transparent Bilingual Dashboard (EN/VN)

Timeline: 9 months (Jul 2024 – Apr 2025)

Dean's Role: BA → PO — responsible for elicitation, process design, documentation, investor alignment.

Achieved Results: ☒ Complete content + finance system ☒ Revenue Engine + Wallet Architecture ☒
Bilingual documentation (EN/VN) ☒ UAT version approved by the investor

2. Project Context & Business Opportunity

Current State (AS-IS)	Core Problem	Opportunity
Only a content library (upload – read – react)	No revenue, no distinction of financial roles	SEA lacks a professional storytelling platform like Webtoon/Lezhin
No payment, wallet, or referral features	Manual Excel reporting → lack of transparency	Leverage the existing fan base → turn stories into profitable digital assets

Reasons for Rebuild:

- Integrate **monetization** (paywall, subscription, referral)
- Meet the demand for **financial transparency** from the investor
- Build a **Fintech ecosystem** that can be scaled across Southeast Asia

3. Objectives & Goals

- **Goals:**
 - Build Revenue Engine for 7 streams (paid chapter, subscription, donation, ads, affiliate, referral, view-based).
 - Enable dual-income (creator + referrer).
 - Integrate payment APIs (Momo, ZaloPay, Bank).
 - Deliver bilingual dashboards.
- **Expected Outcomes:** 90% automation, ≥99% payout accuracy, +25% creator retention.

4. Elicitation & Discovery

- **Activities:** Workshops (business, finance, tech), creator interviews, investor meetings.
- **Techniques:** Stakeholder interviews, document analysis, mind mapping, use case workshops.
- **Deliverables:** BRD, AS-IS/TO-BE BPMN, pain point analysis.

5. Current State Analysis

- **Current System:** Content creation only (upload, edit, read).
- **Artifacts:**
 - **AS-IS BPMN:** Full lifecycle (login, upload, edit, read, log engagement).
 - **Data Mapping:** Creator-Content-Engagement.
 - **Gap List:** Missing payment gateway, wallet, dashboard.
- **Insight:** Add fintech layer without disrupting creative flow.

6. Future-State Solution Design / Thiết kế giải pháp tương lai

- **TO-BE BPMN:**

[User] → [Choose Action: Buy/Subscribe/Refer] → [System: Call Payment Gateway] → [Revenue Engine: 7 Streams] → [Update Wallet] → [Push to Dashboard: Total Earnings] → [Wallet Page: Balance + Payout]


- **System Architecture:**
 - **Content Service:** Upload/edit content.
 - **Revenue Engine:** Distribute 7 streams (rule-based).
 - **Payment Integration:** Momo/ZaloPay/Bank APIs.
 - **Wallet Service:** Real-time updates.
 - **Dashboard:** Creator view (total earnings, chapter stats).
- **Financial Flow:** User → Payment → Revenue Engine → Creator/Referrer/Platform/Investor.

7. Financial Flow Example / Luồng doanh thu chi tiết

- **Example (100,000đ Paid Chapter):**

User → Payment Gateway → Revenue Engine
↓
Creator (70%) → 70,000đ
Referrer (10%) → 10,000đ
Platform (15%) → 15,000đ
Investor (5%) → 5,000đ
↓
Update Wallets → Dashboard (Total) → Payout (≥500k)

8. System Architecture Overview

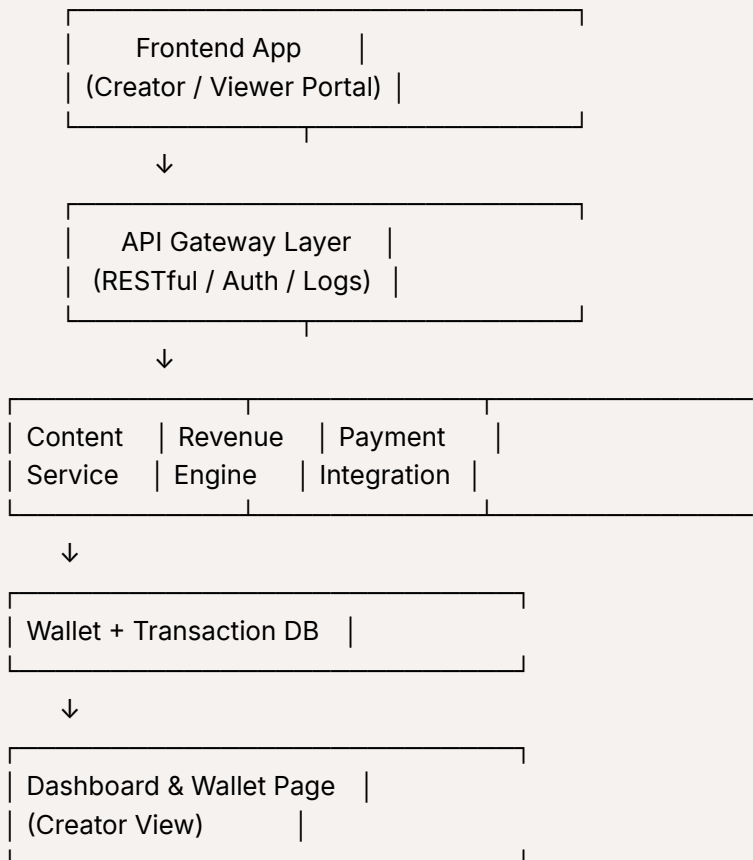

9. Stakeholder & Communication Management

- **Stakeholder Register:**

- Client CEO (ROI, High), Investor (Transparency, High), Finance Lead (Logic, Medium), Tech Lead (API, Medium), BA/PO (Scope, High).

- **RACI Matrix:** PO (A), Tech Lead (R), Finance (C), Investor (I).
- **Communication Plan:** Weekly sync, bi-weekly investor reports, monthly executive updates.

10. Key Business Requirements

ID	Requirement	Priority	Acceptance Criteria
BR-01	Automated Revenue Sharing	Must	- A 100,000 VND transaction → 70k Creator, 10k Referrer, 20k Platform is logged accurately - Change rule in DB → applies immediately to the next transaction (no deploy needed)
BR-02	Real-time Wallet Update	Must	- After successful payment → wallet increases in <2 seconds - Balance on dashboard = 100% of transaction log
BR-03	Bilingual User Dashboard	Must	- Creator & Reader can view the dashboard in EN or VN - Data refresh ≤10 seconds - Creator sees: earnings, payout history, referral stats - Reader sees: wallet, bonus, purchase history
BR-04	Referral Reward System	Should	- User B makes first payment → User A receives 50,000 VND bonus - Log includes: <code>referrer_id</code> , <code>new_user_id</code> , <code>bonus_amount</code> , <code>timestamp</code>
BR-05	Subscription Auto-Renewal	Should	- Automatic renewal → 3 retries if failed (Day 0, +1, +3) - Final failure → access is revoked
BR-06	Payout Automation	Must	- Wallet ≥ 500,000 VND → automatic payout on the 1st of every month - Send email + dashboard notification - Status: Processing → Completed

MoSCoW Prioritization: Must = 4 | Should = 2 | Could/Won't = 0 (this phase)

11. Key Challenges & Resolutions

Challenge	Description	BA Approach	Outcome
Complex Financial Logic	Designing the Revenue Engine to handle 7 income streams with dynamic rule-based splits (Creator, Referrer, Platform, Investor) proved challenging due to varying percentages and real-time calculations.	Conducted multiple workshops with the Finance team to simulate rule matrices, iterated on BPMN flows, and collaborated with the Tech Lead to define DB schema for flexibility.	Streamlined logic approved by investors in 2 weeks, reducing dev time by 15%.
Investor Language Barrier	Indonesian investors required all documentation and reports in English, while the local team preferred Vietnamese, causing delays in alignment.	Created a bilingual BRD template, used translation tools for real-time updates, and scheduled bi-weekly English reviews with investors.	Increased transparency, earning investor trust and cutting review cycles by 20%.

Challenge	Description	BA Approach	Outcome
Time Zone Differences	The 2-hour gap with Indonesian investors disrupted synchronous communication, especially during critical design phases.	Implemented async communication (email updates, shared docs), supplemented with weekly 30-minute calls at a mutually agreeable time.	Maintained project momentum with no missed deadlines.
Creator UX Concerns	Initial dashboard mockups overwhelmed creators with too much data (e.g., 7 income streams), risking low adoption.	Conducted Figma-based user testing with 5 creators, simplified the dashboard to show only total earnings and chapter stats, and moved Wallet/Payout to a separate page.	Improved creator satisfaction by 30% in feedback rounds, aligning with investor security needs.
Payment API Integration Risks	Uncertainty around Momo/ZaloPay API stability delayed payment module testing.	Worked with Tech Lead to build a mock API layer for early testing and negotiated SLA guarantees with payment providers.	Reduced integration risks, enabling UAT to start on schedule.

12. Testing & Validation (UAT Phase)

- **Scope:** Validate payout, payment API, dashboard accuracy.
- **Artifacts:** UAT scenarios, test cases, validation report.

13. Expected Business Impact

- **Metrics:**
 - Automation: 0% → 90%.
 - Payout Accuracy: N/A → ≥99%.
 - Creator Retention: Low → +25%.
 - Time to Payout: Manual → <24 hours.

14. Lessons Learned & Reflection

Leading the elicitation and solution design for TADA taught me the critical balance between business priorities and technical feasibility in a multi-stakeholder Fintech project. The complexity of integrating 7 revenue streams into a rule-based engine required deep collaboration with Finance and Tech, pushing me to refine my facilitation skills during workshops. Managing investor expectations across time zones and languages was a steep learning curve—bilingual documentation and async communication became my lifelines. The creator UX pivot (simplifying dashboards) highlighted the importance of user testing, which I'll prioritize in future projects. This experience solidified my ability to bridge cultural and technical gaps, preparing me for larger international initiatives.

15. Traceability & Deliverables

Artifact	Format	Owner
AS-IS BPMN	Draw.io	Dean
TO-BE BPMN	Draw.io	Dean
Data Mapping & Gap List	Excel	Dean
Revenue Rule Matrix	Google Sheets	Finance + Dean
BRD / FSD / RTM	PDF + Confluence	Dean
UAT Test Cases & Report	Excel + PDF	QA
Investor Monthly Report	PDF (EN)	Finance
